










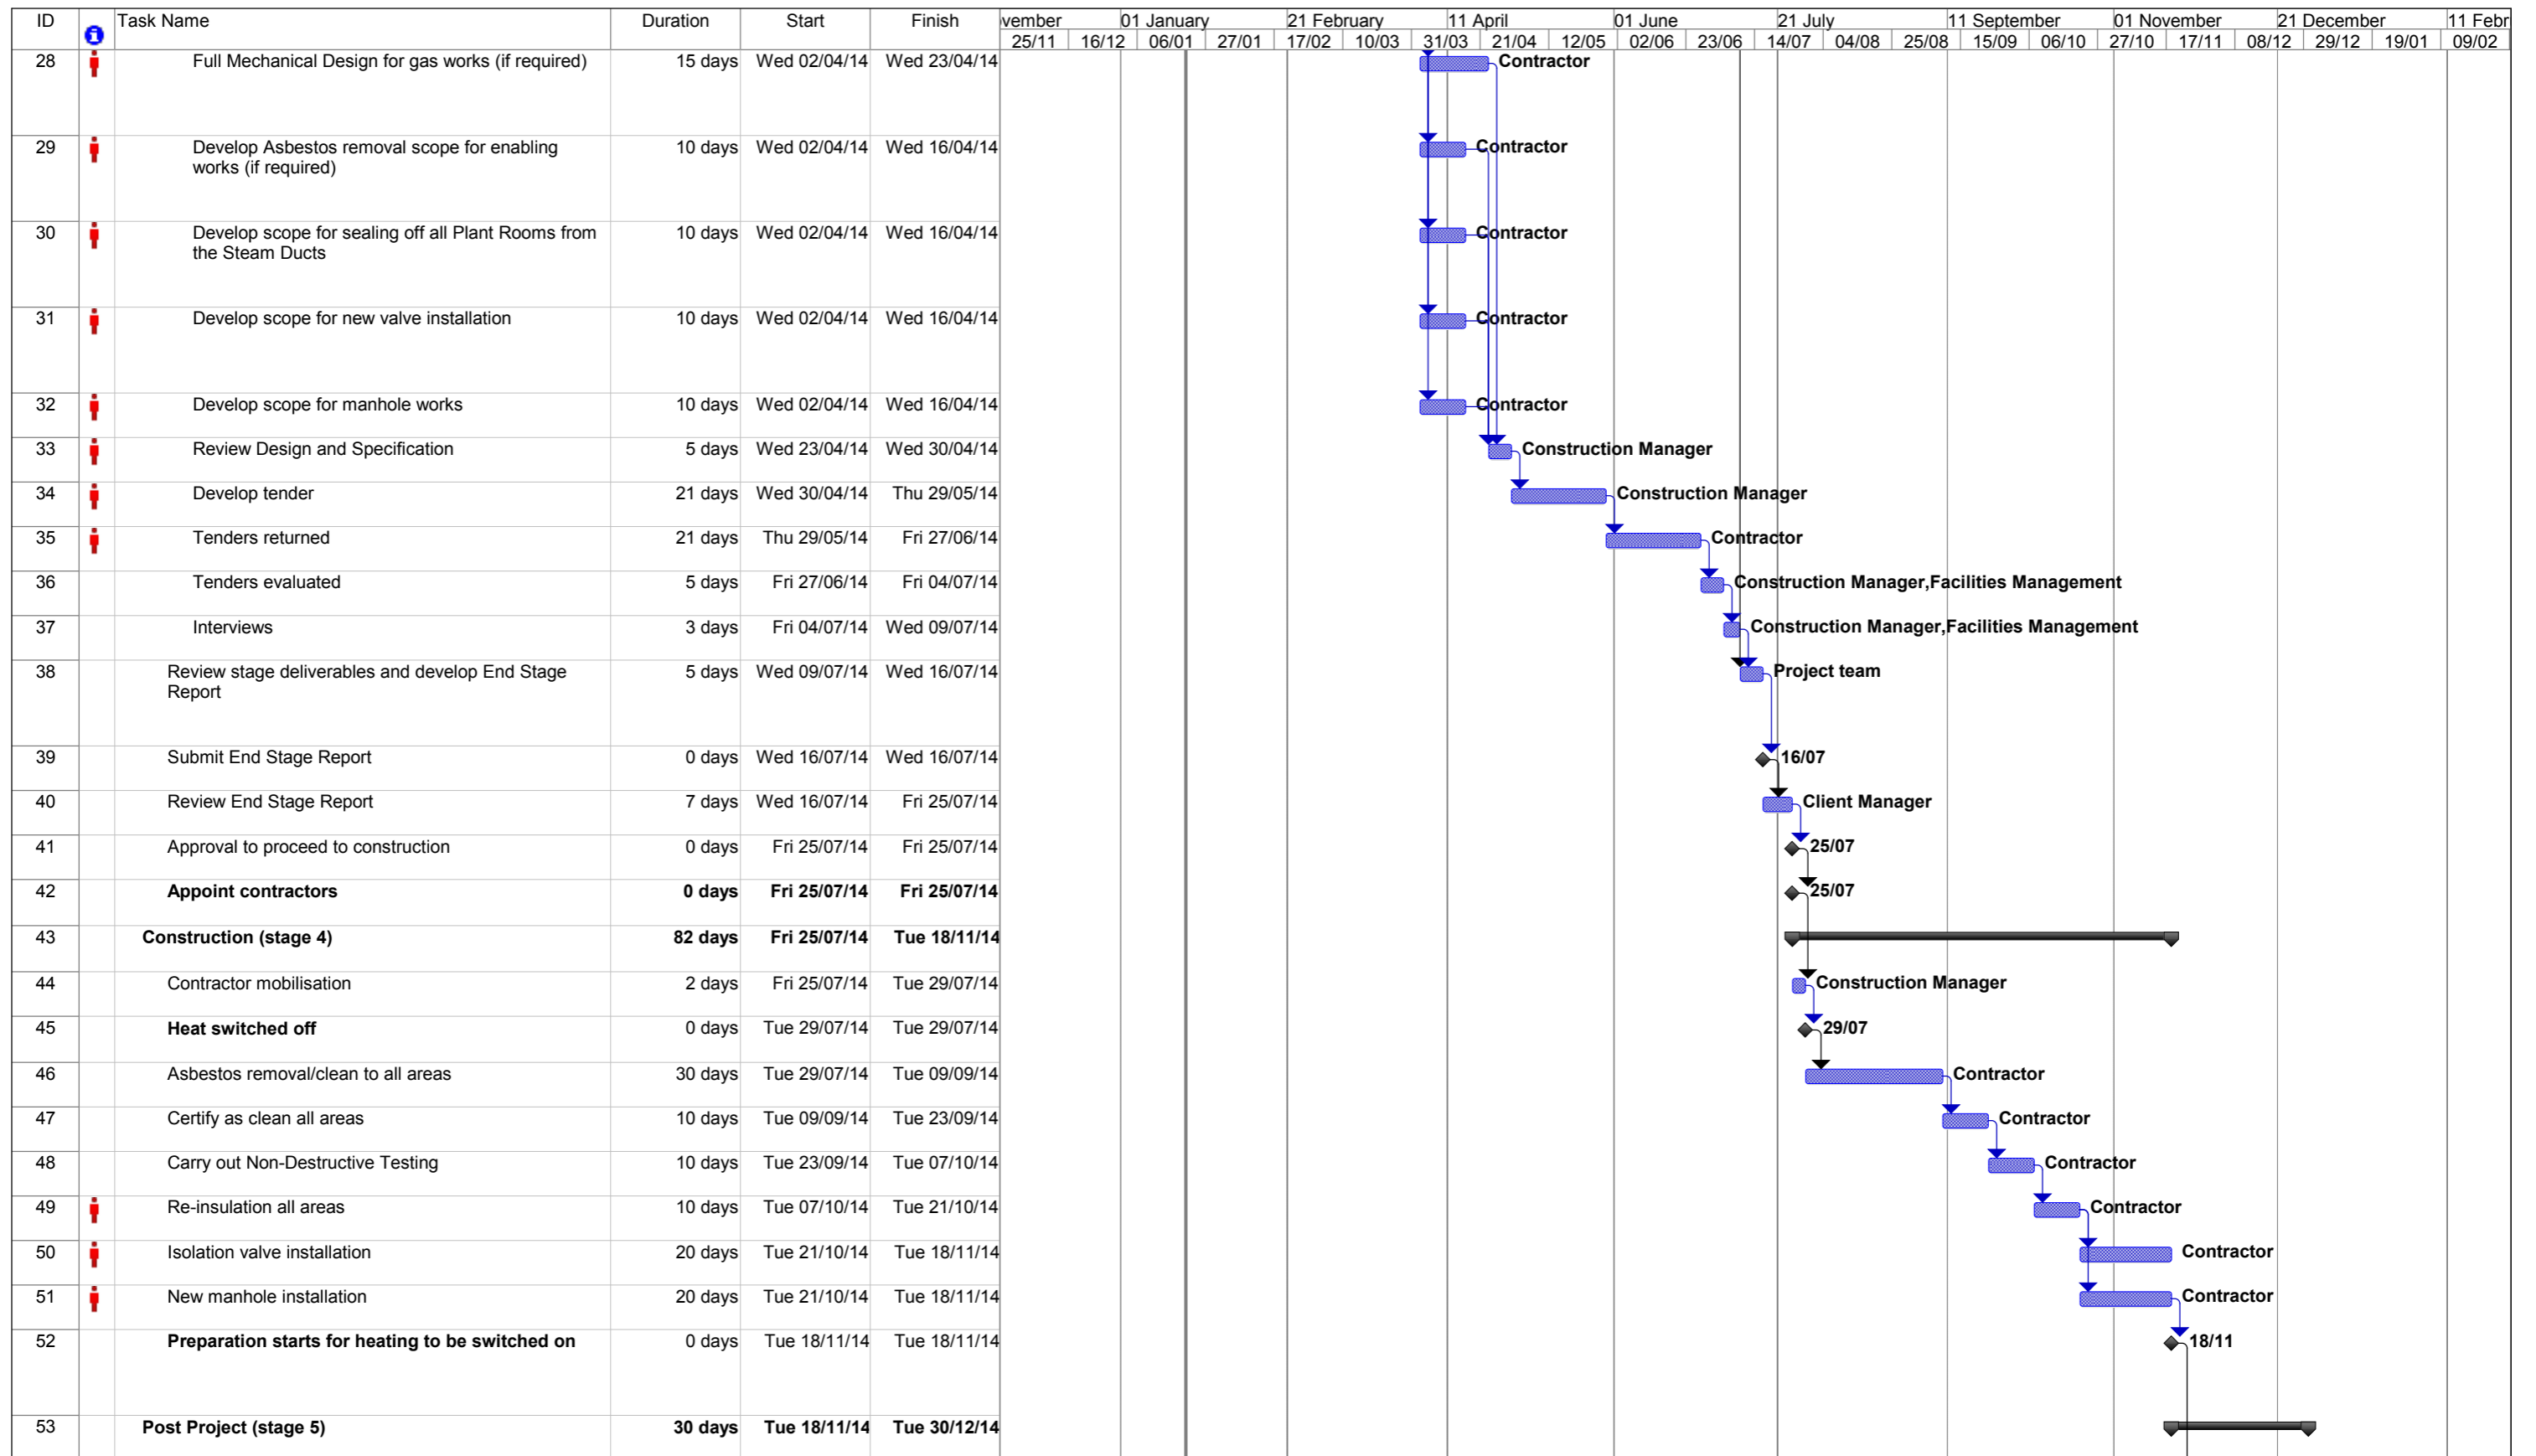















Project: Example Construction Manag Date: Tue 21/01/14	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
	Split		External Tasks		Inactive Summary		Manual Summary		Split	
	Milestone		External MileTask		Manual Task		Start-only			
	Summary		Inactive Task		Duration-only		Finish-only			



Project: Example Construction Manag Date: Tue 21/01/14	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress	
	Split		External Tasks		Inactive Summary		Manual Summary		Split	
	Milestone		External MileTask		Manual Task		Start-only			
	Summary		Inactive Task		Duration-only		Finish-only			

ID	Task Name	Duration	Start	Finish	November		01 January		21 February		11 April		01 June		21 July		11 September		01 November		21 December		11 Febr
					25/11	16/12	06/01	27/01	17/02	10/03	31/03	21/04	12/05	02/06	23/06	14/07	04/08	25/08	15/09	06/10	27/10	17/11	08/12
54	Deliverables in line with Process Map and Small Works Manual	20 days	Tue 18/11/14	Tue 16/12/14																		Project team	
55	Submit End Stage Report	0 days	Tue 16/12/14	Tue 16/12/14																		16/12	
56	Review End Stage Report	10 days	Tue 16/12/14	Tue 30/12/14																		Client Manager	
57	Approval to close the project	0 days	Tue 30/12/14	Tue 30/12/14																		30/12	



Project: Example Construction Manag Date: Tue 21/01/14	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Progress		Split
	Split		External Tasks		Inactive Summary		Manual Summary		Start-only		Finish-only
	Milestone		External MileTask		Manual Task		Duration-only		Task		Task
	Summary		Inactive Task		Task		Task		Task		Task
